




Magnolia Avenue Gateway Monument Project

Project Description: Coincident with the Magnolia Avenue Streetscapes Project, a gateway monument sign will be installed at the northeast corner of E Magnolia Avenue and Jessamine Street.

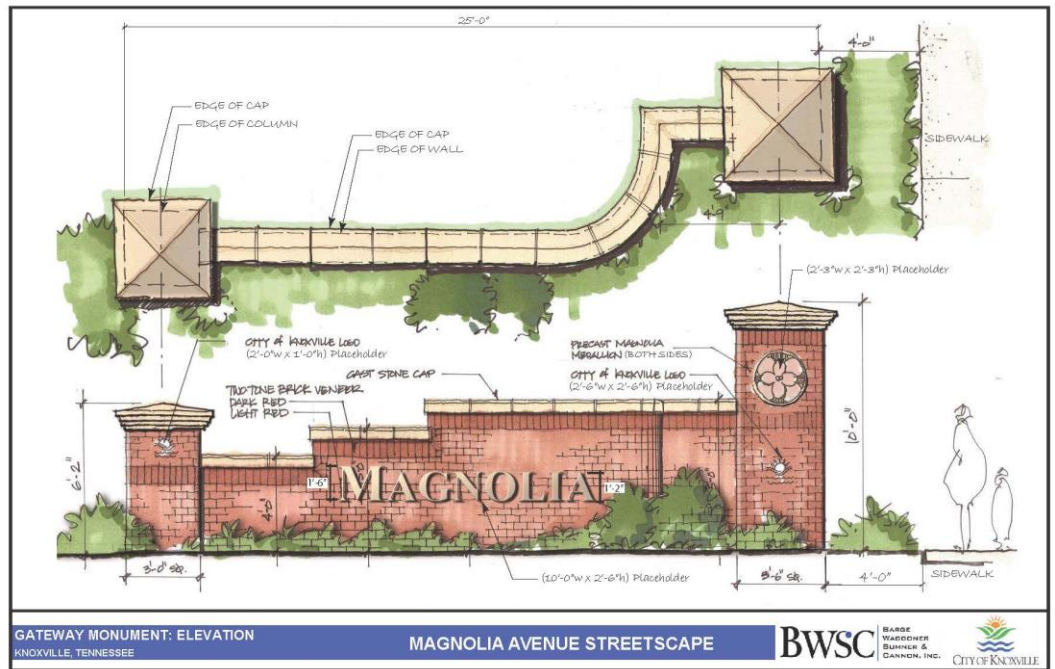

Schedule:

Bid Opening: August 16, 2018
Notice to Proceed: March 4, 2019
Contract Completion Date: April 2, 2019

Current Contract Price: \$ 68,000

Engineering Department June 2019 Status: The project is substantially complete.

Project Designer: Barge Design Solutions, Inc.
Construction Contractor: The Franklin Group, LLC

City of Knoxville Contact
Construction Engineer: Robin L. Tipton, PE (865) 215-6100



CITY OF KNOXVILLE
Madeline Rogero, Mayor

James R. Hagerman, PE
Director of Engineering
