




# 2019 Facilities Paving Project

**Project Description:** This project will resurface two parking lots, a circulation road and a driving track, and seal coat two parking lots. Sites include: City of Knoxville Loraine Street Facility at 1440 Loraine Street, KPD Driving Track at 6388 Cement Plant Road, John T. O'Connor Senior Citizen's Center Parking Lot at Ruth Petersen Place, Lonsdale Parking Lot at East Corner of Stonewall Street and Texas Avenue.

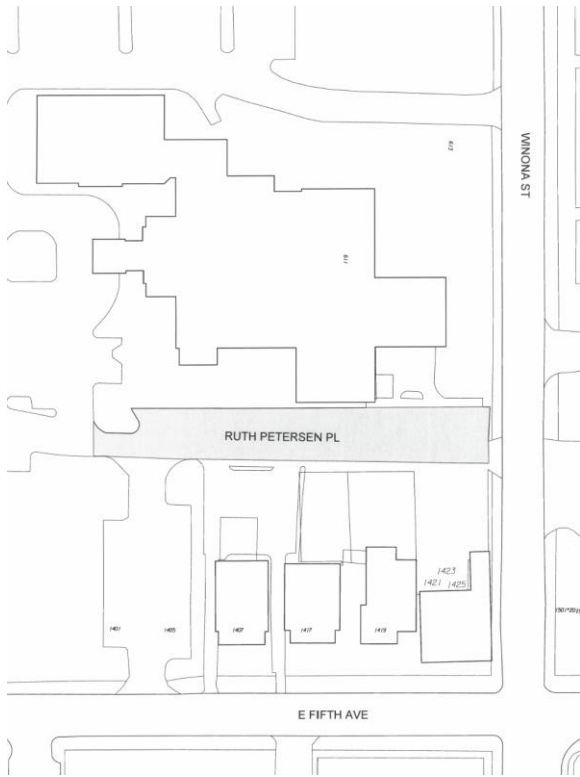

**Schedule:**  
Bid Opening: May 15, 2019  
Notice to Proceed: August 5, 2019  
Contract Completion Date: October 3, 2019

**Current Contract Price:** \$ 597,233

**Engineering Department September 2019 Status:** This construction project was approved at the June 4, 2019 City Council Meeting. The Public Service parking lot, KPD driving track and Lonsdale parking lot are complete.

**Project Designer:** City of Knoxville  
**Construction Contractor:** Duracap Asphalt Paving Company, Inc..

**City of Knoxville Contact**  
**Construction Engineer:** Robin L. Tipton, PE (865) 215-6100



CITY OF KNOXVILLE  
Madeline Rogero, Mayor

James R. Hagerman, PE  
Director of Engineering
