




## 2019 Facilities Paving Project

**Project Description:** This project will resurface two parking lots, a circulation road and a driving track, and seal coat two parking lots. Sites include: City of Knoxville Loraine Street Facility at 1440 Loraine Street, KPD Driving Track at 6388 Cement Plant Road, John T. O'Connor Senior Citizen's Center Parking Lot at Ruth Petersen Place, Lonsdale Parking Lot at East Corner of Stonewall Street and Texas Avenue.

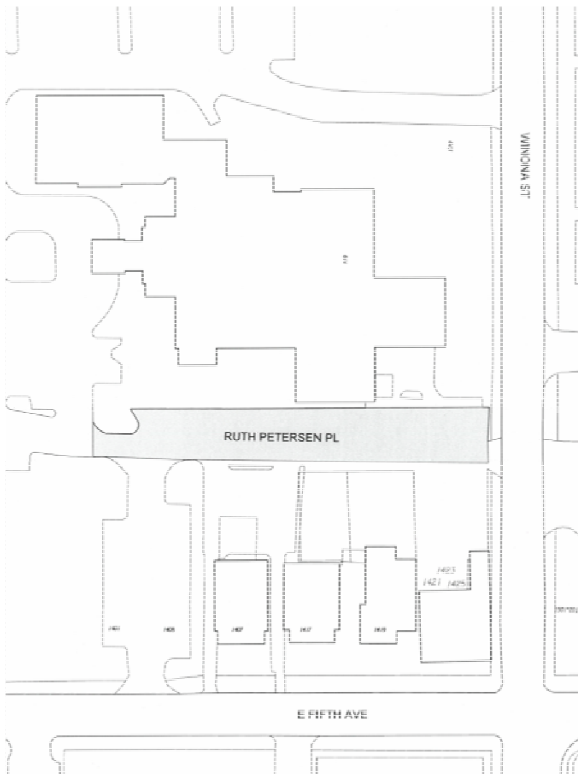

### Schedule:

Bid Opening: May 15, 2019

Notice to Proceed: August 5, 2019

Contract Completion Date: November 2, 2019

**Current Contract Price:** \$ 709,451

**Engineering Department January 2020 Status:** The Public Service parking lot, KPD driving track and Lonsdale parking lot are complete. A Change Order was approved at the September 24, 2019 City Council Meeting to add the resurfacing of employee parking lots at KPD Driving Track and Fire Department Headquarters.

**Project Designer:** City of Knoxville

**Construction Contractor:** Duracap Asphalt Paving Company, Inc.

**City of Knoxville Contact**

**Construction Engineer:** Robin L. Tipton, PE (865) 215-6100



CITY OF KNOXVILLE

Indya Kincannon, Mayor

James R. Hagerman, PE  
Director of Engineering
